Date	03 October 2026
Team ID	**SWTID-2026-7735**
Project Name	**Auto Ticket Classification using Flow Designer**
Maximum Marks	4 Marks

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Sprint	Epic	Story ID	Task / User Story Description	Story Points	Assigned To	Status
Sprint 1	Governance	USN-01	Create & initialize 'Project Update Set' in Local Update Sets	2	ServiceNow Admin	Completed
Sprint 1	Schema	USN-02	Create custom table 'Incident WorkFlow' with Auto Number (INCWF)	3	ServiceNow Admin	Completed
Sprint 1	Schema	USN-03	Configure fields: Caller, Short Description, Description, State	3	ServiceNow Admin	Completed
Sprint 1	Taxonomy	USN-04	Create Category choice list [Network, Hardware, Access, Performance]	2	ServiceNow Admin	Completed
Sprint 1	Taxonomy	USN-05	Create Subcategory choice list and configure Dictionary Dependency	3	ServiceNow Admin	Completed
Sprint 1	Automation	USN-06	Build Flow Designer Trigger (Record Created, Category is Empty)	2	Flow Developer	Completed
Sprint 1	Automation	USN-07	Implement If/Else-If keyword conditions (Wi-Fi, Projector, Password, Slow)	5	Flow Developer	Completed
Sprint 2	Notification	USN-08	Configure Send Email action with dynamic data pills to Caller	3	Flow Developer	Completed
Sprint 2	Automation	USN-09	Activate Flow Designer flow and verify system execution context	2	Flow Developer	Completed
Sprint 2	QA / Testing	USN-10	Execute functional test scenarios (WiFi, Projector, Password, Slow)	5	QA Lead	Completed

Sprint 2	QA / Testing	USN-11	Verify email dispatch in System Logs > Emails (Preview Mail)	3	QA Lead	Completed
Sprint 2	Deployment	USN-12	Mark Update Set Complete, export to XML, compile final deliverables	5	ServiceNow Admin	Completed

Project Tracker, Velocity & Burndown Chart: (4 Marks)

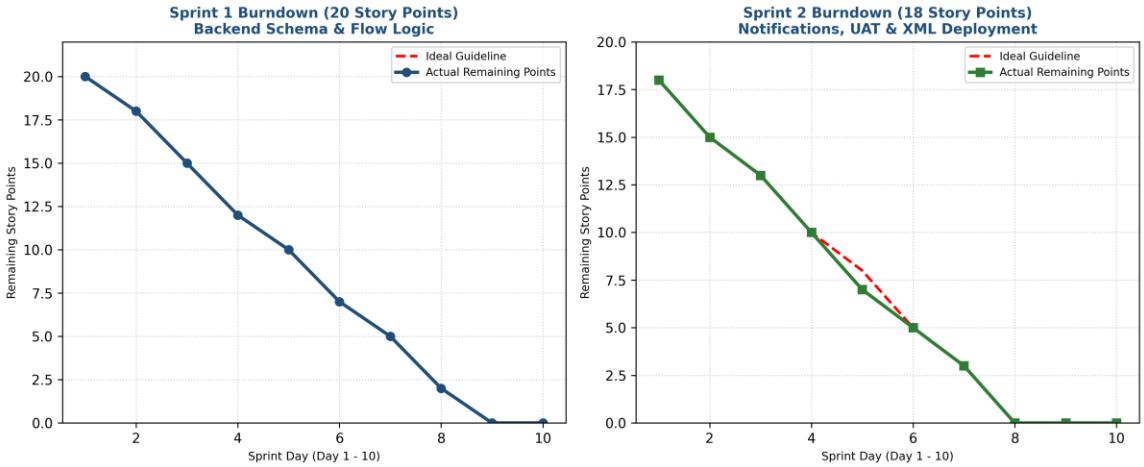


Figure 4.1: Agile Sprint Burndown Tracking for Sprint 1 & Sprint 2

Sprint 1 Burndown Tracking (20 Story Points):

Sprint Day	Planned Remaining	Actual Remaining	Completed Tasks	Status
Day 1	20	20	Sprint Planning & Backlog Refinement	On Track
Day 2	18	18	USN-01: Update Set created	On Track
Day 3	15	15	USN-02: Custom Table & Auto Number created	On Track
Day 4	12	12	USN-03: Fields & Data types provisioned	On Track
Day 5	10	10	USN-04: Category choice lists loaded	On Track
Day 6	7	7	USN-05: Subcategory dependent dictionary mapped	On Track
Day 7	5	5	USN-06: Flow trigger configured & tested	On Track
Day 8	2	2	USN-07 (Part 1): Wi-Fi and Projector logic built	On Track
Day 9	0	0	USN-07 (Part 2): Password & Performance logic built	Ahead

Day 10	0	0	Sprint 1 Review, Demo, and Retrospective	Completed

Sprint 2 Burndown Tracking (18 Story Points):

Sprint Day	Planned Remaining	Actual Remaining	Completed Tasks	Status
Day 1	18	18	Sprint 2 Planning & Target Alignment	On Track
Day 2	15	15	USN-08: Send Email action configured	On Track
Day 3	13	13	USN-09: Flow activated in Flow Designer	On Track
Day 4	10	10	USN-10: Scenario 1 (WiFi) & Scenario 2 (Projector) validated	On Track
Day 5	8	7	USN-10: Scenario 3 (Password) & Scenario 4 (Slow PC) validated	Ahead
Day 6	5	5	USN-11: System Logs > Emails inspection verified	On Track
Day 7	3	3	USN-12: Update Set state set to Complete	On Track
Day 8	0	0	USN-12: Export to XML & artifact validation	Completed
Day 9	0	0	Final documentation review and sign-off	Completed
Day 10	0	0	Final Project Submission & Presentation	Completed
